




SINGLE STOCK FUND

Milestones 1 and 2 Implementation Strategy

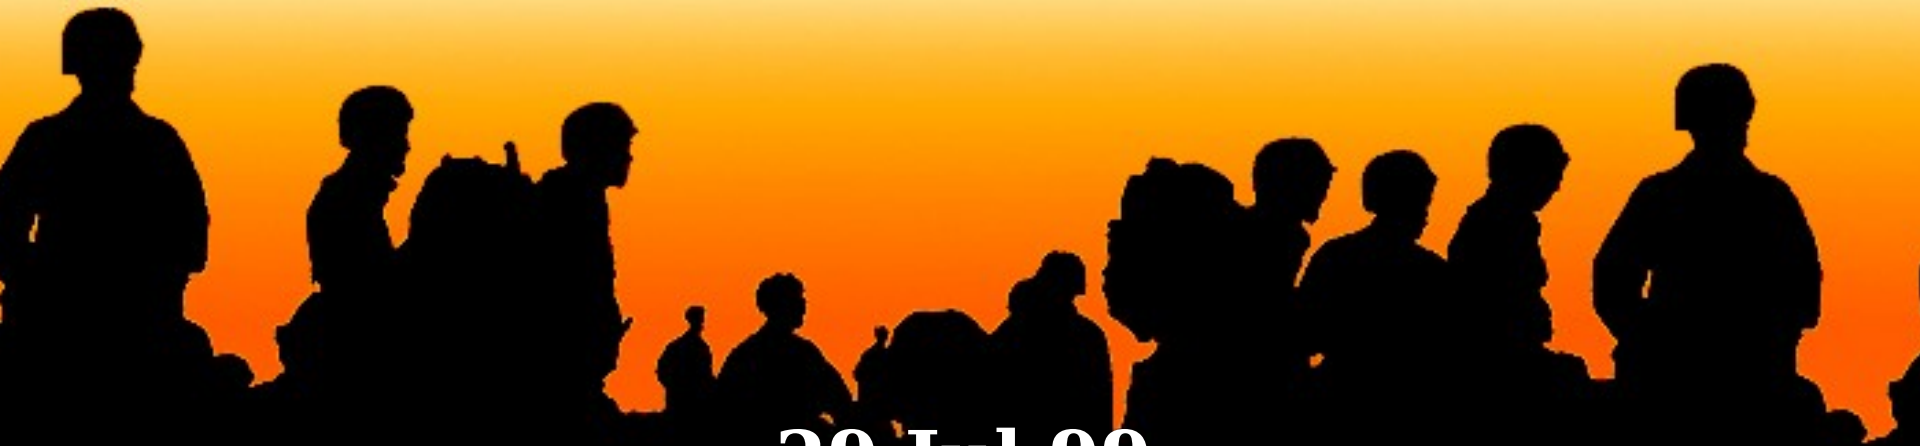

29 Jul 99



Outline

- **Background**
- **Actions/Events Since the Last GOW**
- **Implementation Requirements/Time**
- **Revised MS-1-2 Schedule**
- **Detailed Implementation Plan Deve**




Definition

Implementation: All events, including conversion, to ensure Army-wide institutionalization of the Single Stock Fund Conc



SARSS-1 & AMCISS Sites (USA)

Milestone 1 AND 2

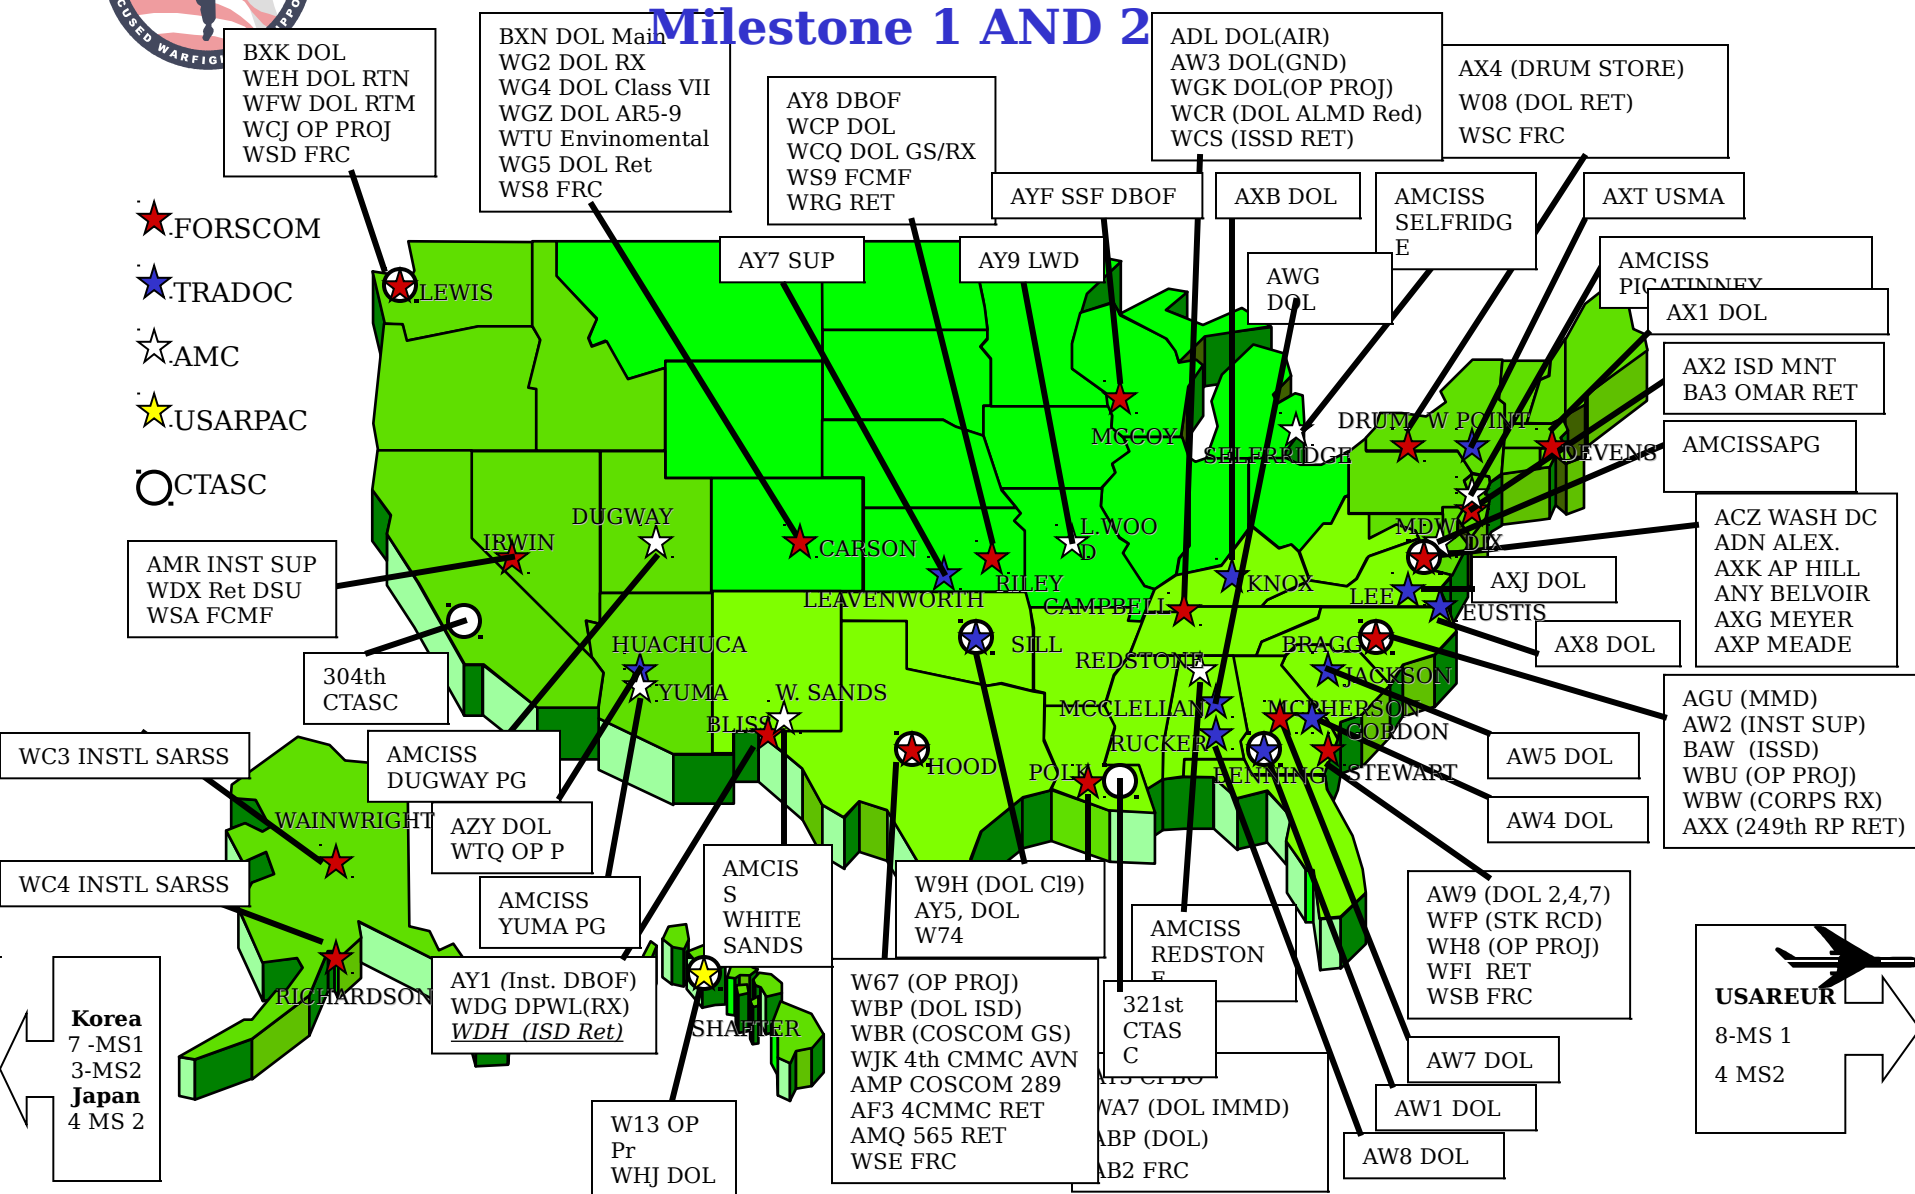




SARSS-1 & AMCISS Sites


Milestone 1 and 2

★ SARSS-1
○ CTASC

Korea

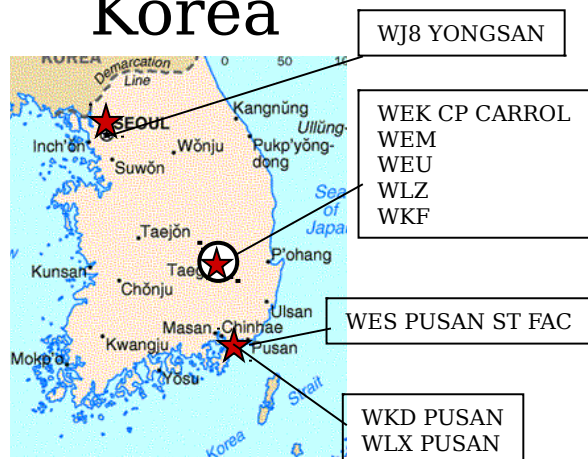

Japan

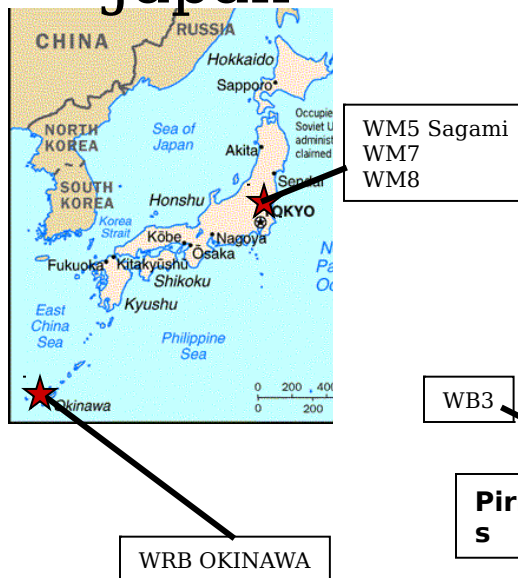

Germany






Where We Were-Last GOWG Conversion Plan MS 1-2 Combined

Demo In Apr-Jun 00

Ft. Sill
~~Presidio of Monterey~~
~~Ft. Lewis~~
Ft. McPherson
Redstone Arsenal
Converted in FY00

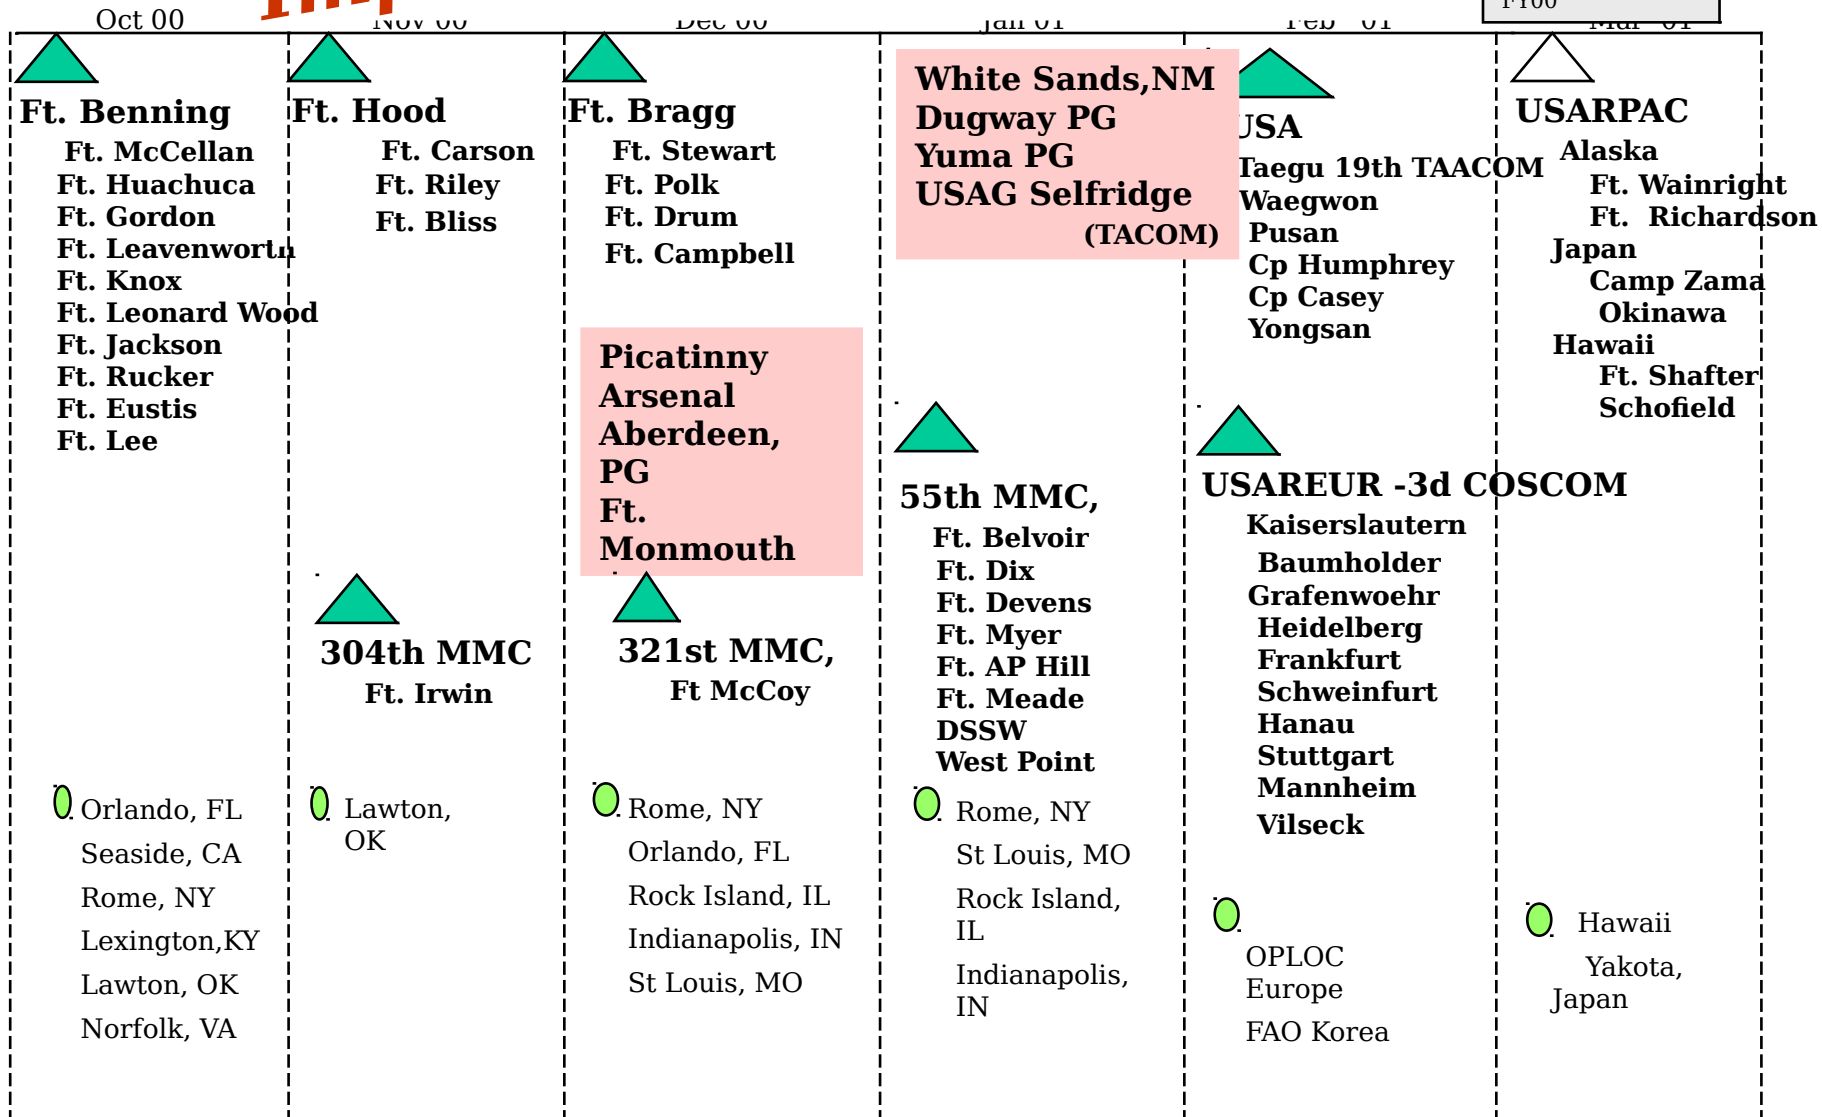



Since the Last GOWG...

- **Road Shows: FORSCOM, TRADOC, & Ft. Br**
- **MS 2 Implementation Procedure Workshop**
- **Consideration of Conversion Schedules Opti**
- **Consideration of MS 1-2 Sequential**
- **Continued Shared/Dedicated CTASC Analysis**
 - **Disconnect/Reconnect trials Lab/Live com**
 - **Parameter Evaluation workshop 1st two w**
- **VTC with MACOMs - July 9**

**WE ARE
WORKING YOUR
CONCERNS!**




Milestone 2 Course of Action

From MS 2 Workshop May 18-20

- **COA**
 - **Capitalize O&M retention/redistribution stocks IAW consolidated (MS1&2) fielding schedule**
- **Supporting Tasks**
 - **Turn off the process that moves all serviceable excess to OMA Retention SARSS-1 boxes**
 - **Examine local repair programs and where economical, incorporate into NMM repair program**
 - **Consolidate multiple storage sites with AWCF-SMA SARSS-1 boxes, when feasible:**
 - **Link to current Phase-in Plan, 1 Oct 00 through Mar 01**
 - **Expand current conversion plan (Supply)**
 - **As additional requirements are identified for MS2, detailed justification will be submitted to ASAFM-BUO-O and BUR for consideration**
 - **Reduce number of AWCF SARSS-1 boxes overtime**




What Gets Converted To SSF-When??

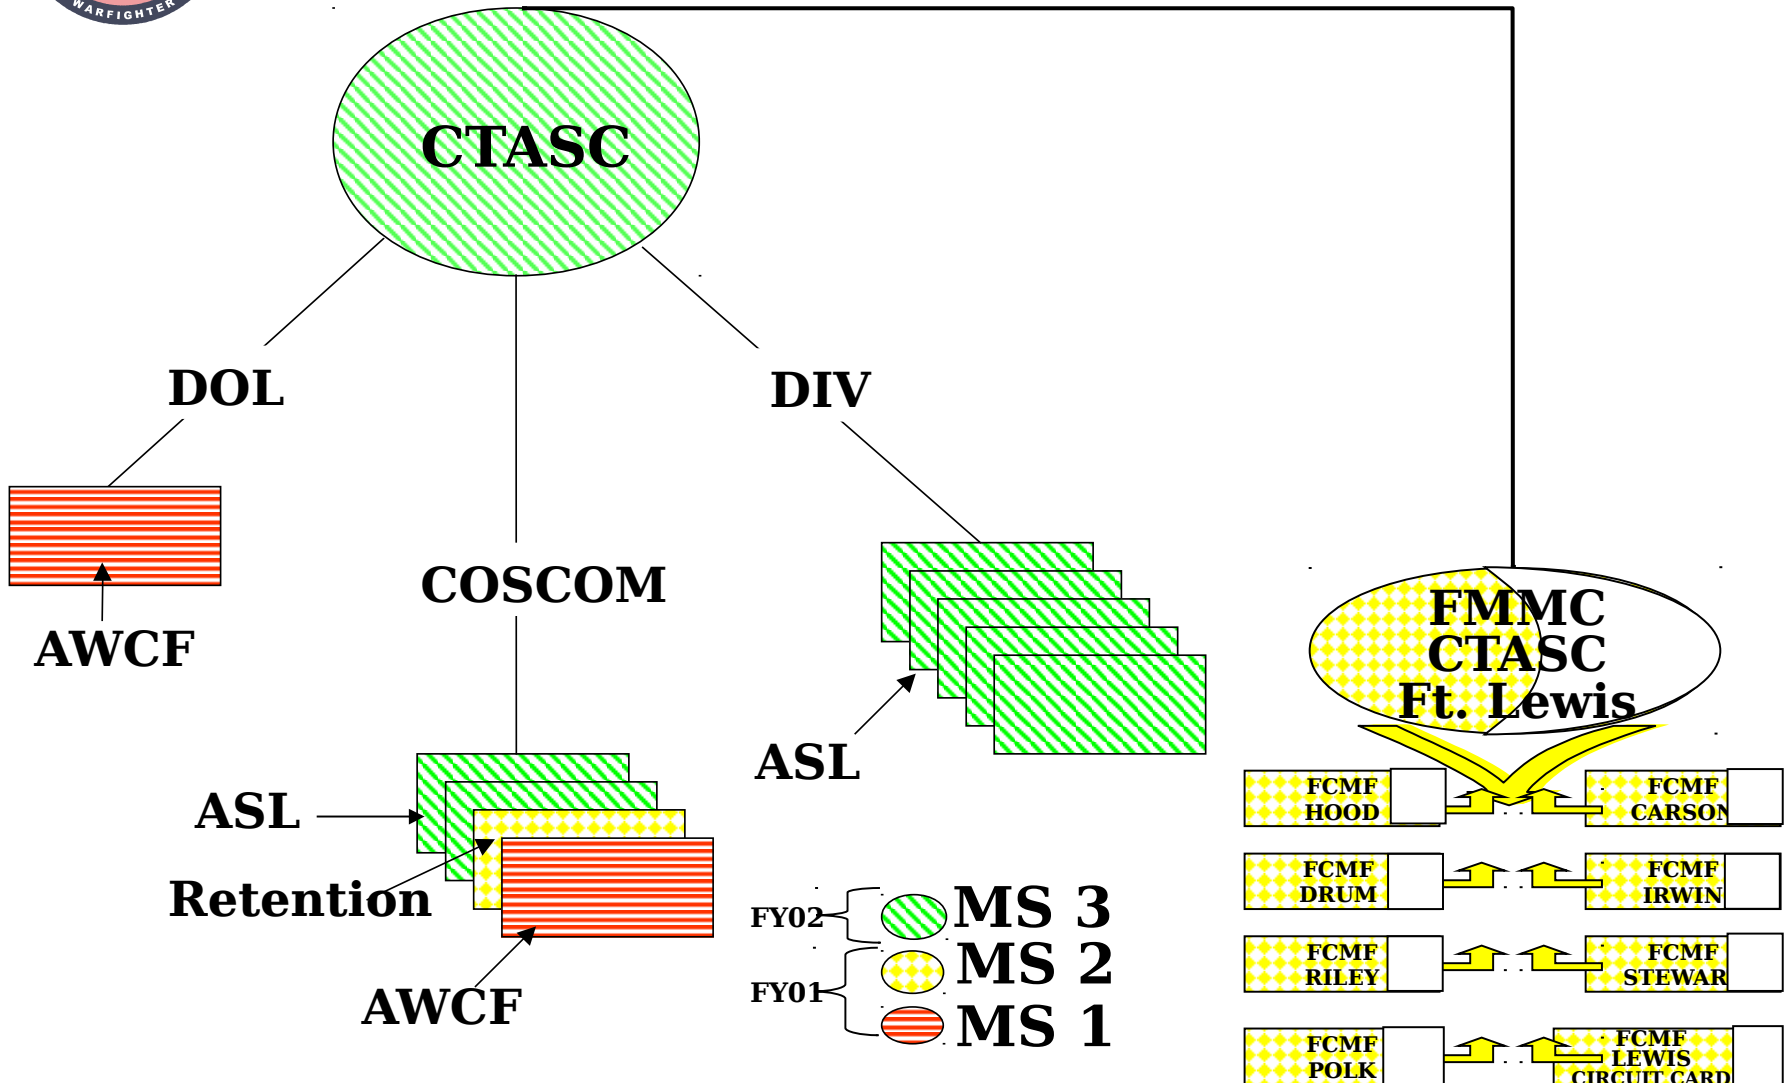



Retention/FMMC Stock Consolidation

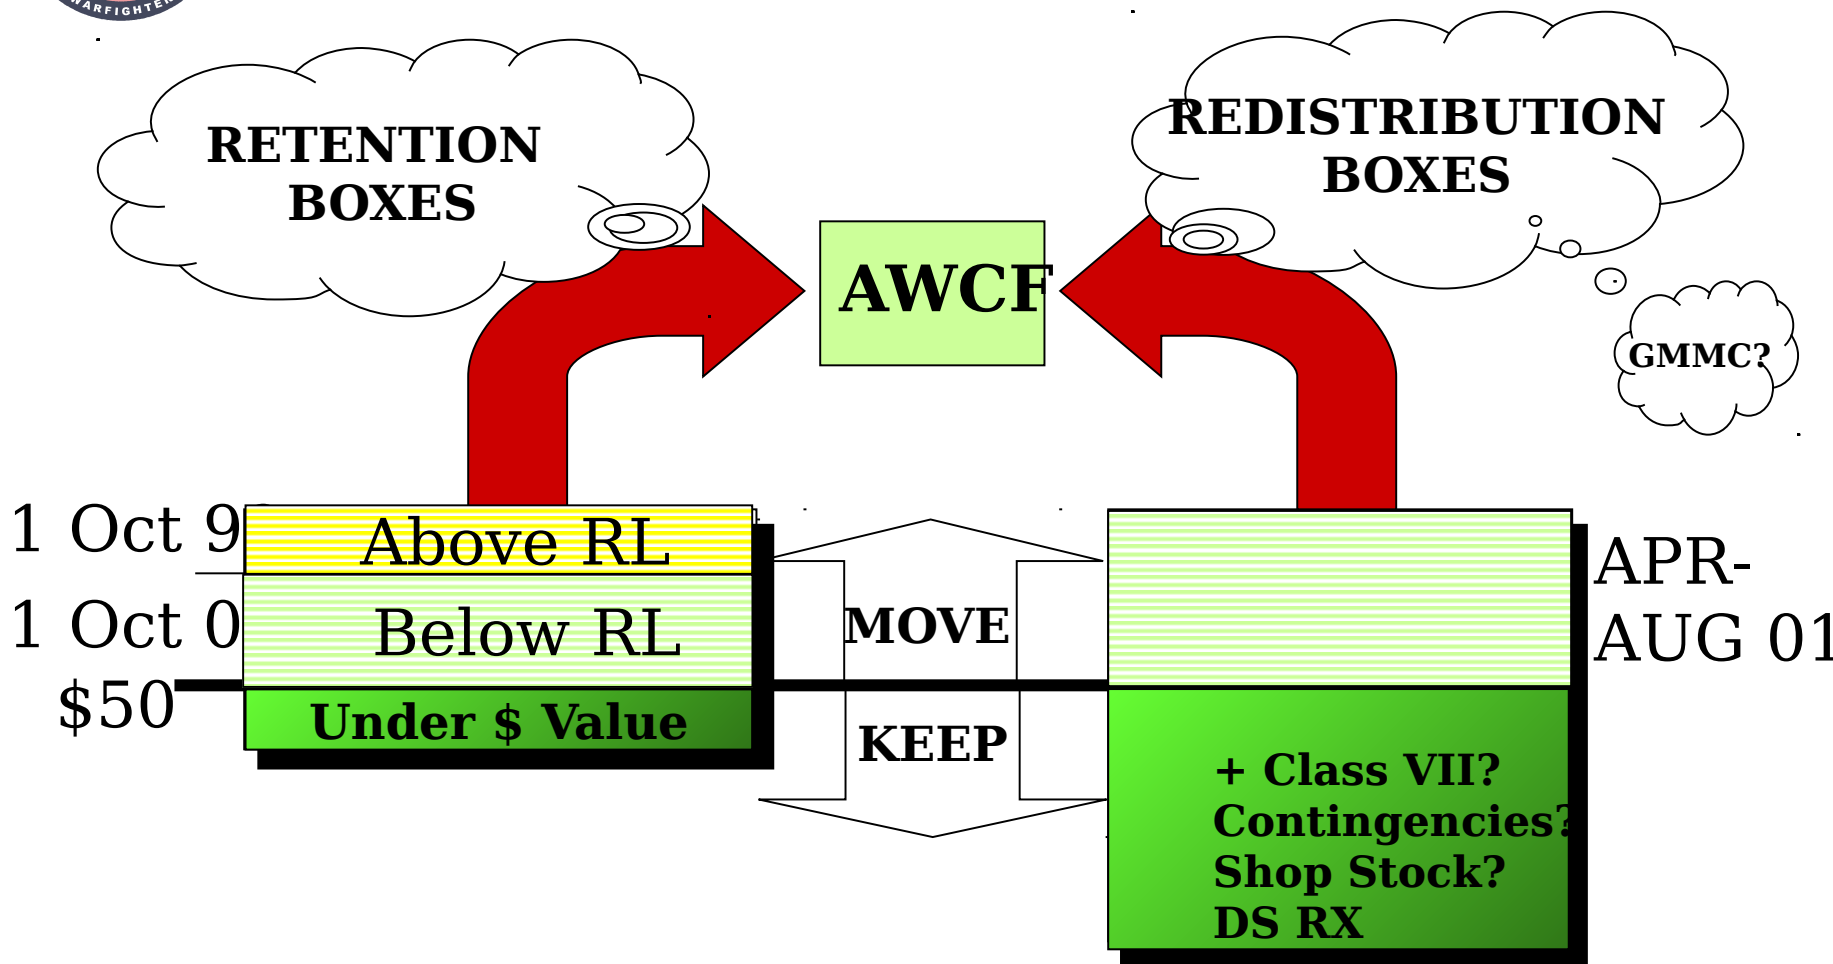

Installation Tailored based on IP Team Recommendation

Option 1 Stocks move to AWCF, boxes remain OMA.

Option 2 Boxes move to AWCF, stocks move to OMA



Where to From Here??

STEP 1:

Determine Policy

Determine RO/RL Timing
Determine Exclusions \$500

STEP 2:

Sizing the Xf
Inventory

Survey Large Retention Lo
-FMMC Sites
-Europe

IP Team

STEP 3:

Determine SARSS
Box Reductions

Determine SARSS 1 Reduc
Strategy By Site/Timing
-Move Stocks ?
-Move Boxes ?
-Leave As Is ?



Revised Implementation Schedule

Guiding Principals

- **Event Driven -**
 - **MS-1(+) (ASLs plus retention boxes) in first half of FY 01,**
 - **MS-2 (-) (redistribution boxes) in 2d half**
- **MACOM Integrity - Conversion by CTASC**
- **Situationally Responsive - Modified IAW integrated process team recommendations**



Revised

Implementation Schedule (C-Day)

MS 1-2 Event Sequenced

MS 1(+)

Oct 00	Nov 00	Dec 00	Jan 01	Feb 01	Mar 01
Ft. Benning-O Ft. McCellan-R Ft. Huachuca-Se Ft. Gordon-Lex Ft. Leavenworth-R Ft. Knox-Lex Ft. Leonard Wood-Law Ft. Jackson-R Ft. Rucker-O Ft. Eustis-N Ft. Lee-Law (Ft Sill (-)** Presidio, CA - Law)	Ft. Hood-Law* Ft. Carson-Law* Ft. Riley-Law* Ft. Bliss- Law* (Ft. Sill (-)** Presidio, CA-Law) 304th MMC Ft. Irwin -Law* Ft Lewis (-) Ft. McPherson	Ft. Bragg-R* Ft. Stewart-R* Ft. Polk-O* Ft. Drum-O* Ft. Campbell-R* Ft. Monmouth-St (CECOM) Picatinny Arsenal- USAG Selfridge-St (TACOM) 321st MMC, Ft McCoy-I	Aberdeen PG-RI Dugway PG-RI White Sands, NM- RI Yuma PG-RI 55th MMC St. Belvoir-R Ft. Dix-I Ft. Devens-I Ft. Meade-R MDW/DSSW-I West Point-R	EUSA (FAO Korea) Taegu 19th TAACOM* Waegwon Pusan Cp Humphrey Cp Casey Yongsan USAREUR(Europe OPLOC) Kaiserslautern * Baumholder Grafenwoehr Heidelberg Frankfurt Schweinfurt Hanau Stuttgart Mannheim Vilseck	USARPAC-Pearl Alaska Ft. Wainwright-H Ft. Richardson Japan Camp Zama-Y Okinaw-Y Hawaii Ft. Shafter-H Schofield-H USARSO TBD

MS 2 (-)

Apr 01	May 01	Jun 01	Jul 01	Aug 01
FT Stewart FMMC Ft Drum FMMC Ft Hood FMMC	Ft Polk FMMC Ft. Irwin FMMC	Ft Carson FMMC USAREUR Redist.		Ft. Riley FMMC USARPAC

Retention boxes as determined best value by IP team

GMMC?

Ft. Sill
Ft. Lewis
Redstone Arsenal
Implemented in Apr 99
Demonstration

* Indicates with Retention Boxes

** Depends on Shared vs Dedicated

OPLOCs

I-Indianapolis
Law-Lawton
Lex-
Lextington
N-Norfolk
O-Orlando
R-Rome
RI- Rock
Island
Se-Seaside
St-St. Louis
Yokohama
H-Hawaii



Implementation Detailed Event Timeline

C-90: DFAS schedule STARFIARS-MOD training for OPLOC Conversion

Teams

C-90: Site Survey

C-83: Installation Training

C-60: Installation conduct preliminary supply-finance reconciliation

C-60: OPLOC Conversion Team arrives at installation supporting OP

C-30: CCSS-Finance OPLOC visits installation's STARFIARS-MOD

C-45: Installation SARSS reporting process for serviceable

C-45: Disconnect/Reconnect Actions

C-45: Middleware installation & Testing

C-15: Black-out on physical turn-in's

C-15: CCSS-Finance commences running billing 3 times per week

C-15: CCSS-Finance waives 7-day waiting period till conversion

C-10: Brown-out of normal requisitions

C-10: Installation wall-to-wall inventory with supply/finance recon completed

C-7: OPLOC Conversion Support Team arrives at CCSS-Finance OPLOC

C: Conversion of Installation Retail Stock Fund to SSF

C: Post-post issue transactions from brown-out period

C+3: STARFIARS-MOD OPLOC produces standard month-end AWCF reports


C+30: STARFIARS-MOD OPLOC produces final installation AWCF reports

C+30: OPLOC Conversion Team departs installation supporting OPLOC

**Many Events
For Each Conversion Site.
Each Requiring
Coordinated/integrated
Scheduling**




Typical Implementation Event Schedule For Each CTASC

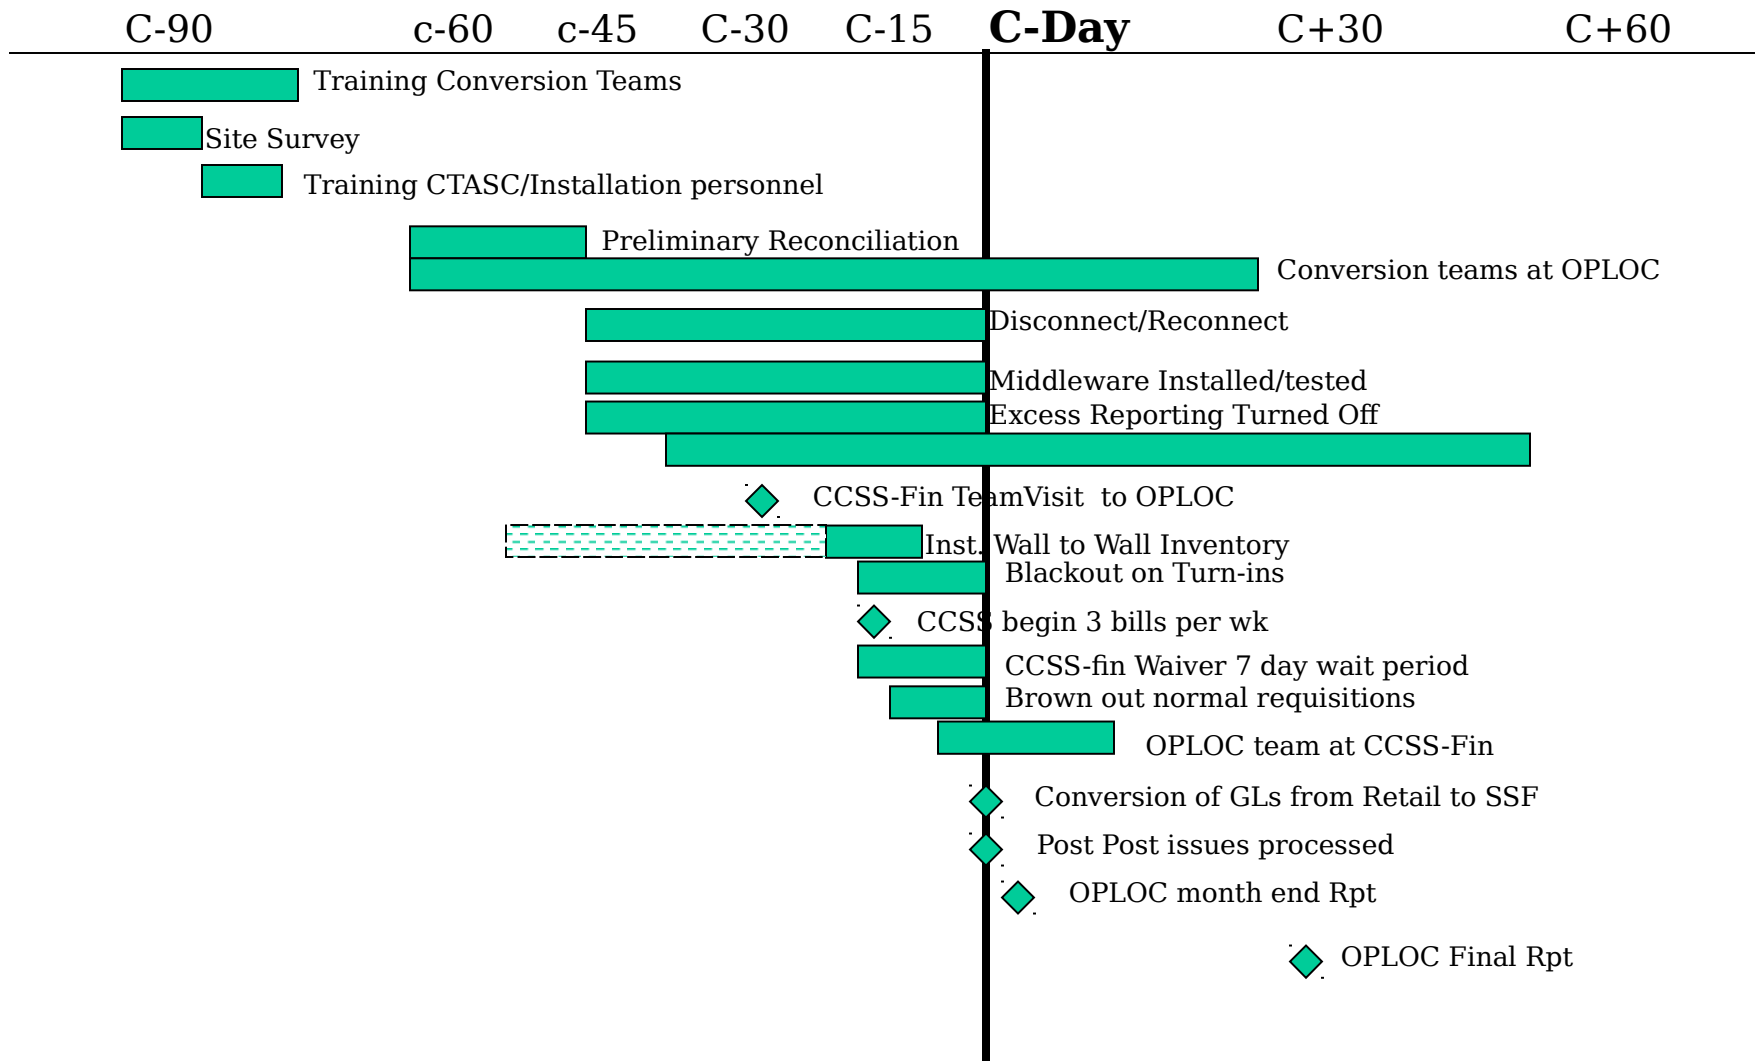



Implementation Timeline

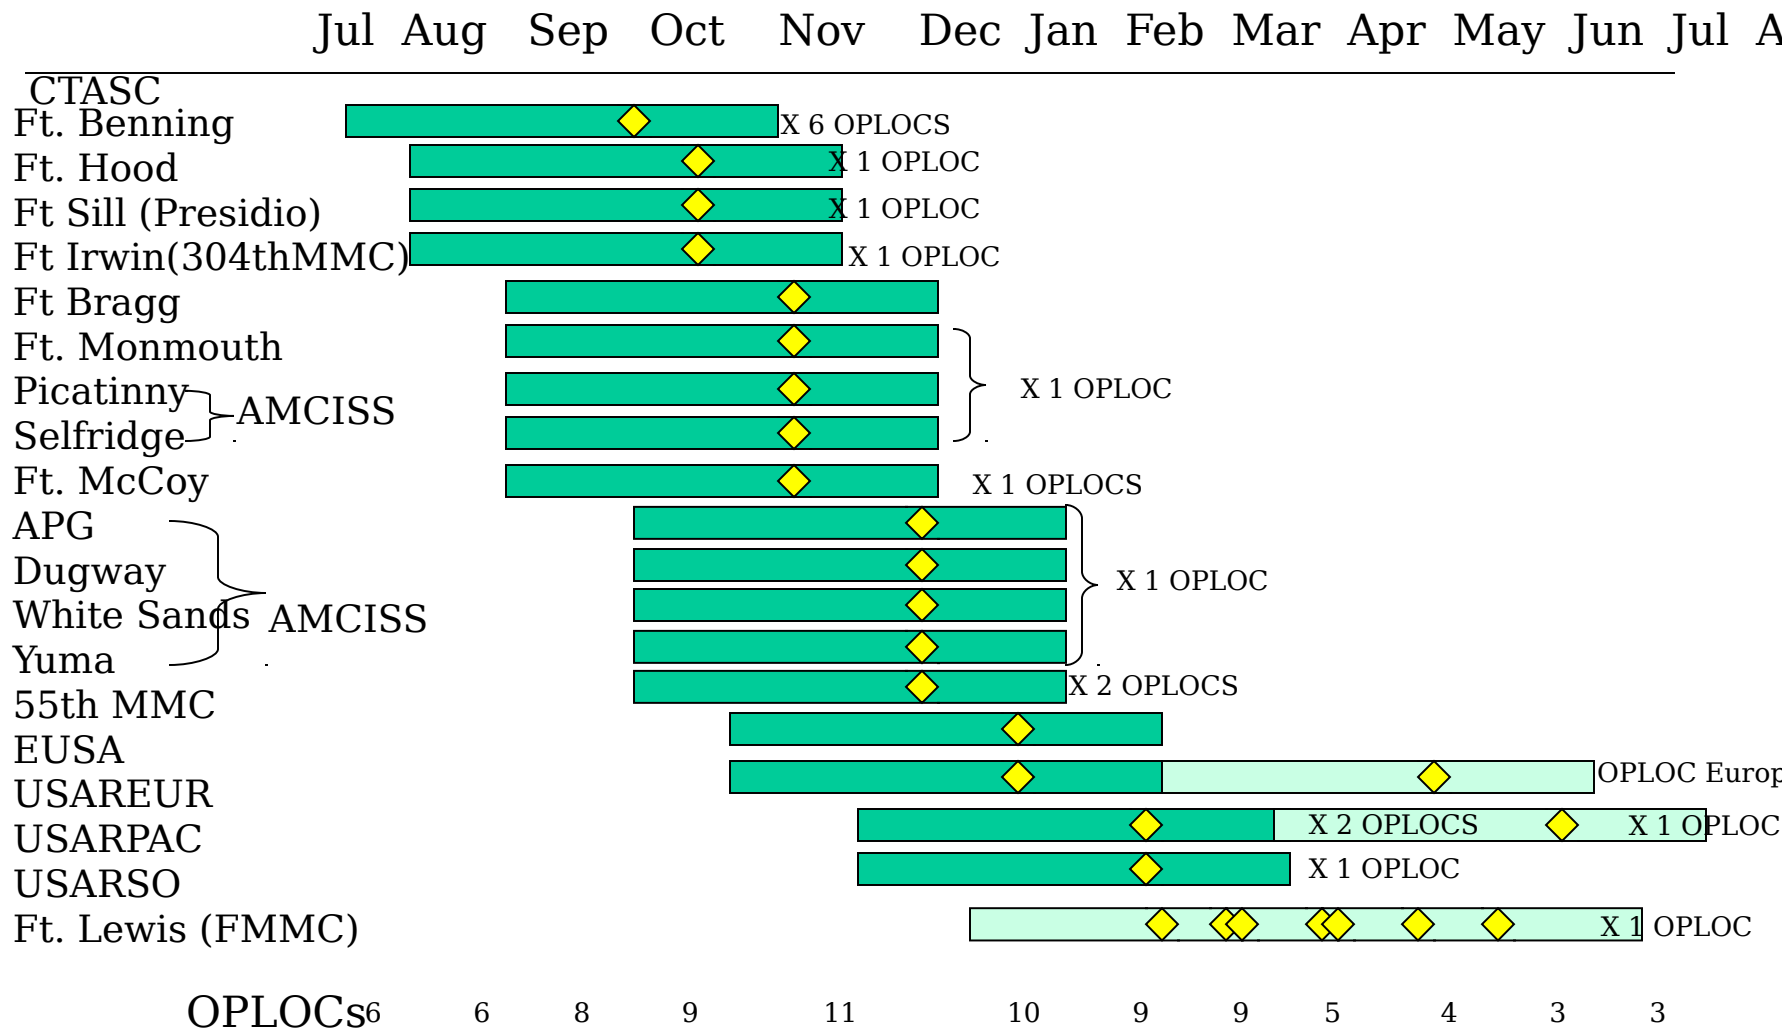



The Next Steps

Planning/Coordination/Publication of Detailed Implementation Plan

Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul A

Concept/Policy★

Structure



IP Team Survey



First Draft



Coordination



Demo Working Draft



Final Draft



Publication



Revisions

.....

Implementation





Summary / Conclusions

- Detailed Planning Ongoing ICW MACC
 - Meetings/Workshops
 - IP Team
 - Staffing
- More Details at Next GOWG
- Final Plan -May 2000
